

## BMP-02: McCormack Pump Station Upgrades

### General description

Installation of a new communitor at the McCormack PS. The new communitor will replace a bar screen system which was ineffective in preventing large diameter debris from entering the wet wells of the PS, especially during wet-weather events.

### Purpose

Increase pump reliability and efficiency.

#### SPDES Permit#

NY-002 5747

#### LTCP Estimated Project Cost (Millions)

\$0.08

#### Grant Funding or other sources

#### Cost-share

\$0.080

#### Maintain

Albany Water Board

#### Own

Albany Water Board

#### Certification

Albany Water Board

#### Manage construction

Albany Water Board

#### Operation

Albany Water Board

#### Enforcement

Albany Water Board

#### Outfall#

A-016

#### Affected Waterbodies

Normanskill Creek, Hudson River

#### Annual Volume Captured (Mgal)


0.0000

#### Consent Order Milestones

Construction Completion Date: 9/30/14

Operational Start-Up Date: 9/30/14

#### Project Location

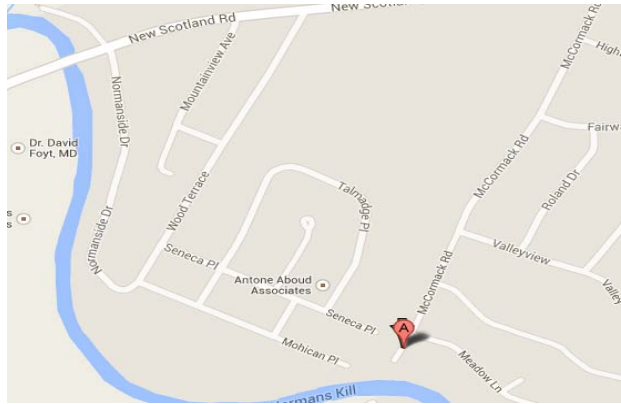

#### Contact Information

Albany Water Board

William Simcoe

(518) 434-5300 / [wsimcoe@albanyny.gov](mailto:wsimcoe@albanyny.gov)

#### Annual Percent CSO Reduction (%)

0.0000

#### Date Milestone Met

9/30/2014

9/30/2014

### Status

**2/18/14:** Awaiting parts for Comminutor and installation of pumps. Has been through board of contract and supply and will be put out to bid. **3/27:** Put out to Bid 4/8/14, with Bids due 4/22/14. **4/24:** Bids have been received. A recommendation for the low bid on the Comminutor was made to the water board. The bid needs to be reviewed by the board of contract and supply before being awarded. **5/12:** Bid has been reviewed by Board of Contract and supply and was awarded. **5/22:** Contract signed, Communitor ordered, expected ship date is June 15th, if shipped on time expected completion by the first of July. **7/10:** Parts received and anticipate full installation by 9/1. **8/14:** Installation underway anticipated completion date of 9/30. **9/10:** The comminutor has been installed and project completion expected on 9/30. **11/13:** Project has been completed and certified.
