


SSS-06
Mariette Place Stormwater Storage Facility
City of Albany

Consent Order Milestones	Date Milestone Met
Completed Plans & Specifications: 10/1/16	9/28/16
NTP to Construction: 4/1/17	3/31/16
Construction Completion Date: 12/15/18	6/1/17
Operational Start-Up Date: 12/15/18	6/1/17

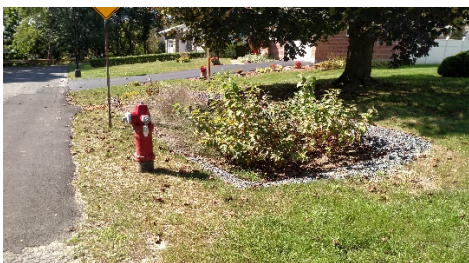

SPDES Permit #s	NY-0025747
LTCP Projected Project Cost (Millions)	\$0.350
Total Construction Cost (minus in-kind)	\$253,109
Owned By	City of Albany
CSO Outfall No.	A-13
Grant Funding or other sources	None
Annual Volume Captured (Mgal)	2MG
Annual Percent CSO Reduction (%) (Pool-Wide)	.05%

Project Description:

Connection of catch basins in the Mariette Place vicinity to a storage facility to reduce peak flows conveyed to the CSS.

Purpose:

Reduces local flooding and reduces both the incidence and frequency of combined sewer discharge to the surface, as well as reducing the frequency and intensity of CSO events.

Contact Information:

Albany Water Board
 William Simcoe
 (518) 434-5300 / wsimcoe@albanyny.gov

Project Status:

7/14/16: The Water Board has retained Barton & Loguidice for design of this project.

10/16: Plans and specs for this project were submitted to DEC for review in September.

3/1/17: DEC issued approval of plans and specs on December 27, 2016. The project went out to bid on February 7. March 7 is the anticipated selection date for contactors. Although categorized in the LTCP as a Sewer Separation project, the Mariette Place project will incorporate Green Infrastructure elements and discharge stormwater in to a vegetated swale.

9/15/17: The project was completed on 7/27/17. Certification of project completion was submitted on 8/13/17.

This project is complete.
