

TE-02 Cross St. Trunk Sewer Rehabilitation Phase I

General description

Replacement of approximately 2,000 linear-feet of 24-inch sewer in the vicinity of Wynants Kill Way. Required limits of repair and/or replacement is currently being evaluated.

Purpose

Repairs will reduce infiltration and improve conveyance capacity thus reducing the frequency and volume of CSOs during wet weather conditions. The project will also reduce exfiltration and associated risks of bacterial contamination during dry-weather conditions.

SPDES Permit#

NY-009 9309

LTCP Estimated Project Cost (Millions)

\$0.64

Grant Funding or other sources

Cost-share

\$0.64

Maintain

City of Troy

Own

City of Troy

Manage construction

City of Troy

Operation

City of Troy

Enforcement

City of Troy

Outfall#

T-045

Affected Waterbodies

Wynants Kill, Hudson River

Certification

Troy

Consent Order Milestones


Construction Completion Date: 12/15/14

Operational Start-Up Date: 12/15/14

Annual Volume Captured (Mgal)

0.0000

Project Location

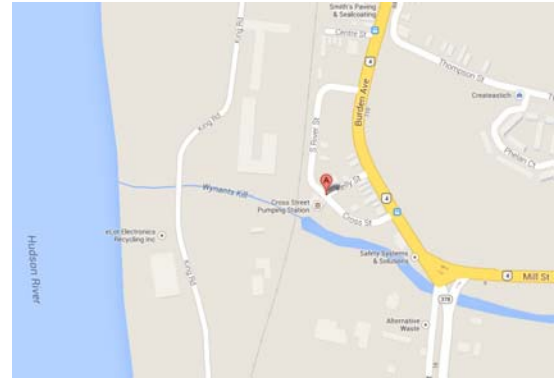

Contact Information

Chris Wheland

City of Troy Public Utilities

(518) 237-0438 / Chris.Wheland@troyny.gov

Date Milestone Met

12/15/2014

12/15/2014

Annual Percent CSO Reduction (%)

0.0000

Status

3/27/14: On schedule. No update at this time. **4/24:** The city anticipates excavation to begin on April 28th. **5/22:** Out of the 2000 ft. line replacement there is about 300 ft. to go, then awaiting clearance from DEC move on to project TE-01.
7/10: TE-02 is for the Wynantskill sewer replacement is nearly complete. **7/24:** Minus some trees to be planted in the fall, complete. Sewer work is done and the new sewer is operational. The old sewer has been decommissioned. **9/11:** When work on the project is completed, the City will submit a certificate. **10/9:** This project is proceeding well ahead of schedule and completion is anticipated very shortly. **11/13:** This project is complete. Certificate will be filed shortly.
1/08/14: Project completed and certified.
